




SPV of SUDA & SMC



**URBAN RING DEVELOPMENT CORPORATION
LIMITED, SURAT**

Outer Ring Road Layout

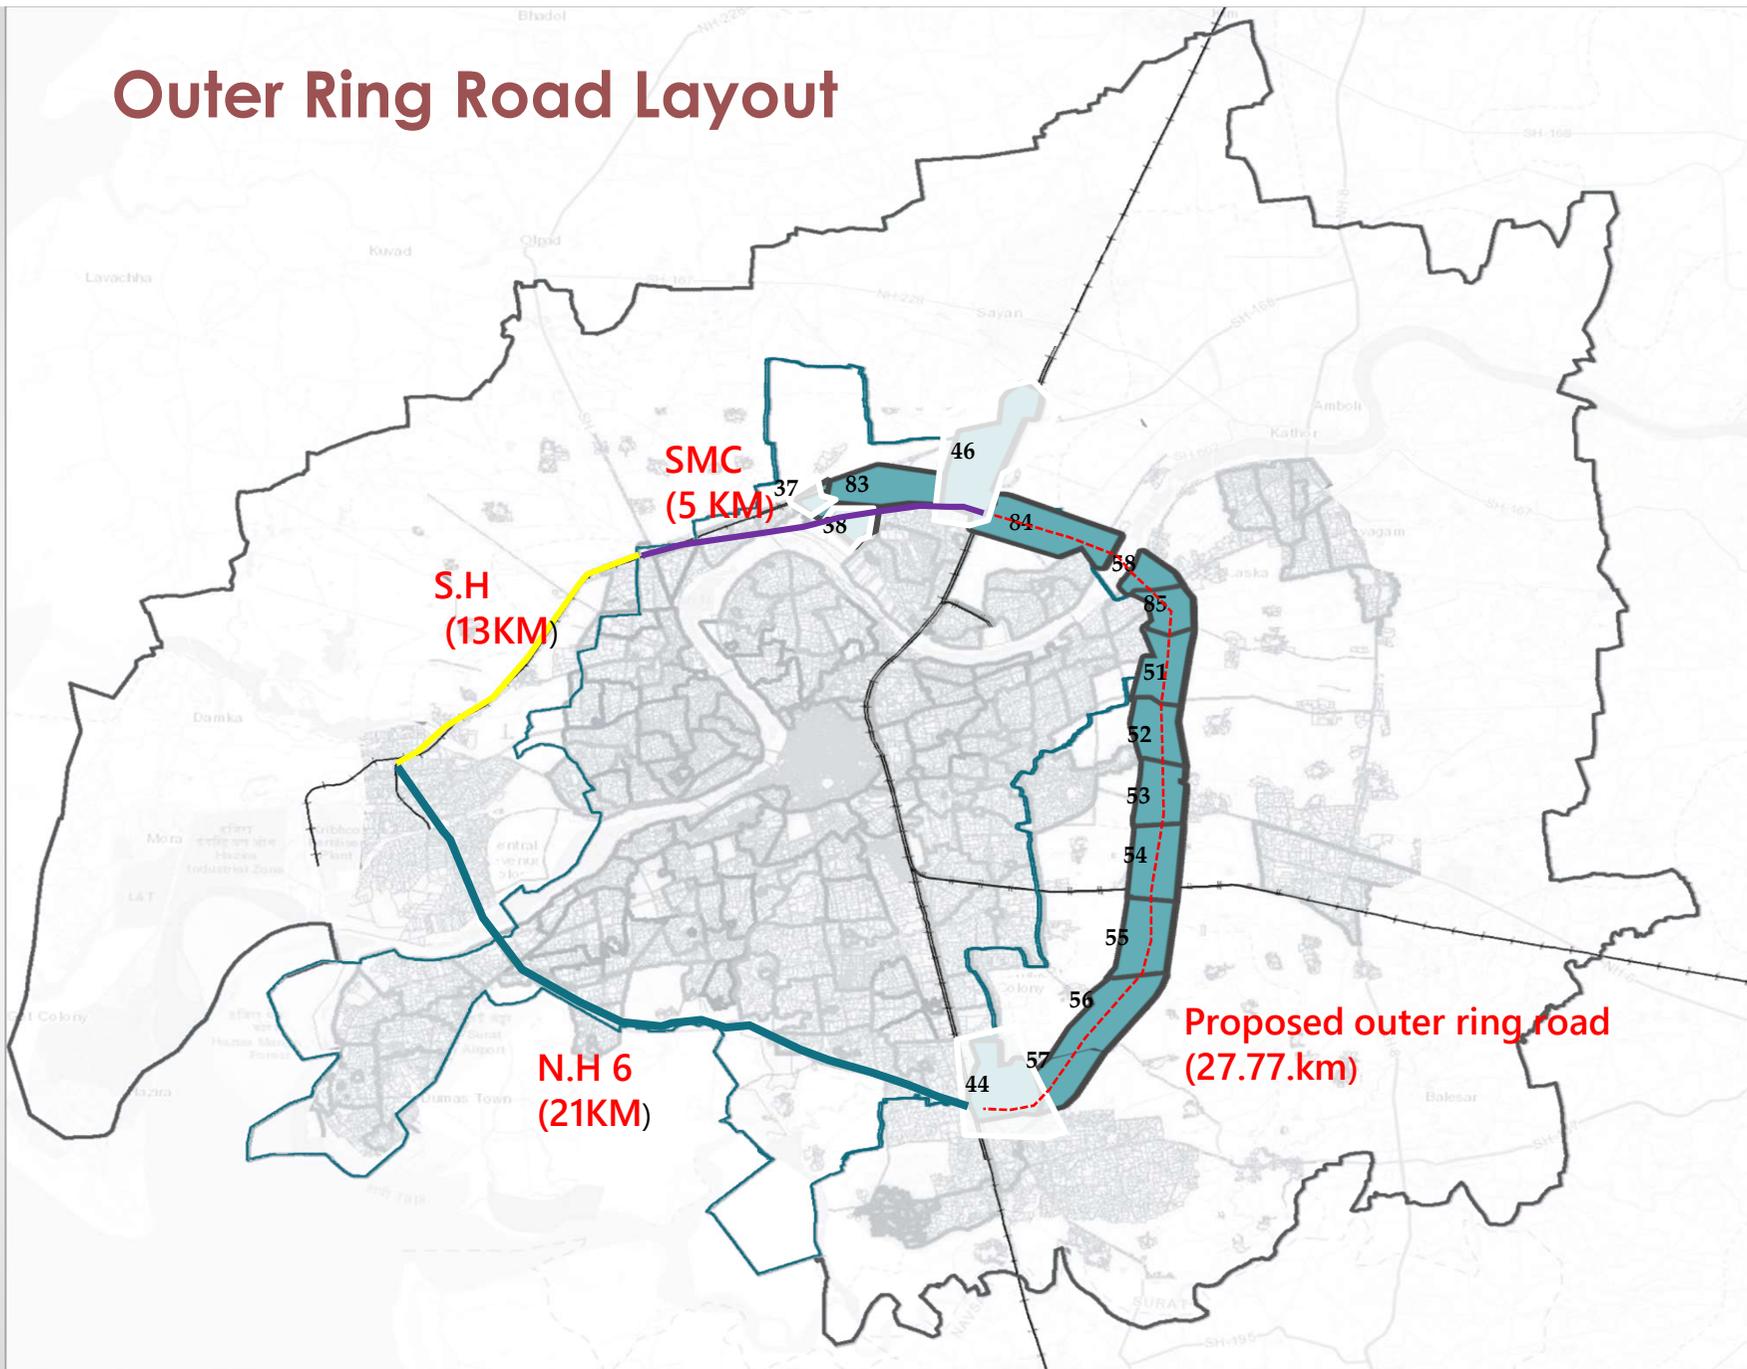

Objective: “Proposed development of Outer Ring Road Surat shall act as development corridor by creating additional GDP. This shall include opportunity for High Speed Transit Corridor. This shall improve accessibility and will have significant increase in revenue from property and professional tax. ”


Existing part of ORR



Phase-01 Proposed Green field development

- **Total Length of the Project : 66.77 km**
 - Existing Outer Ring Road (ORR) Length : 39.00 km
 - Proposed Outer Ring Road (ORR) Length : 27.77 km
- **Length of ORR (Under Execution Phase(1A)) : 17.32 km**
 - Tender Project Cost : 486 Cr.
- **Tentative Schedule for Phase(1A) completion**
 - Road Packages – June 2022
 - Structure Packages – Dec 2022


Surat Outer Ring Road

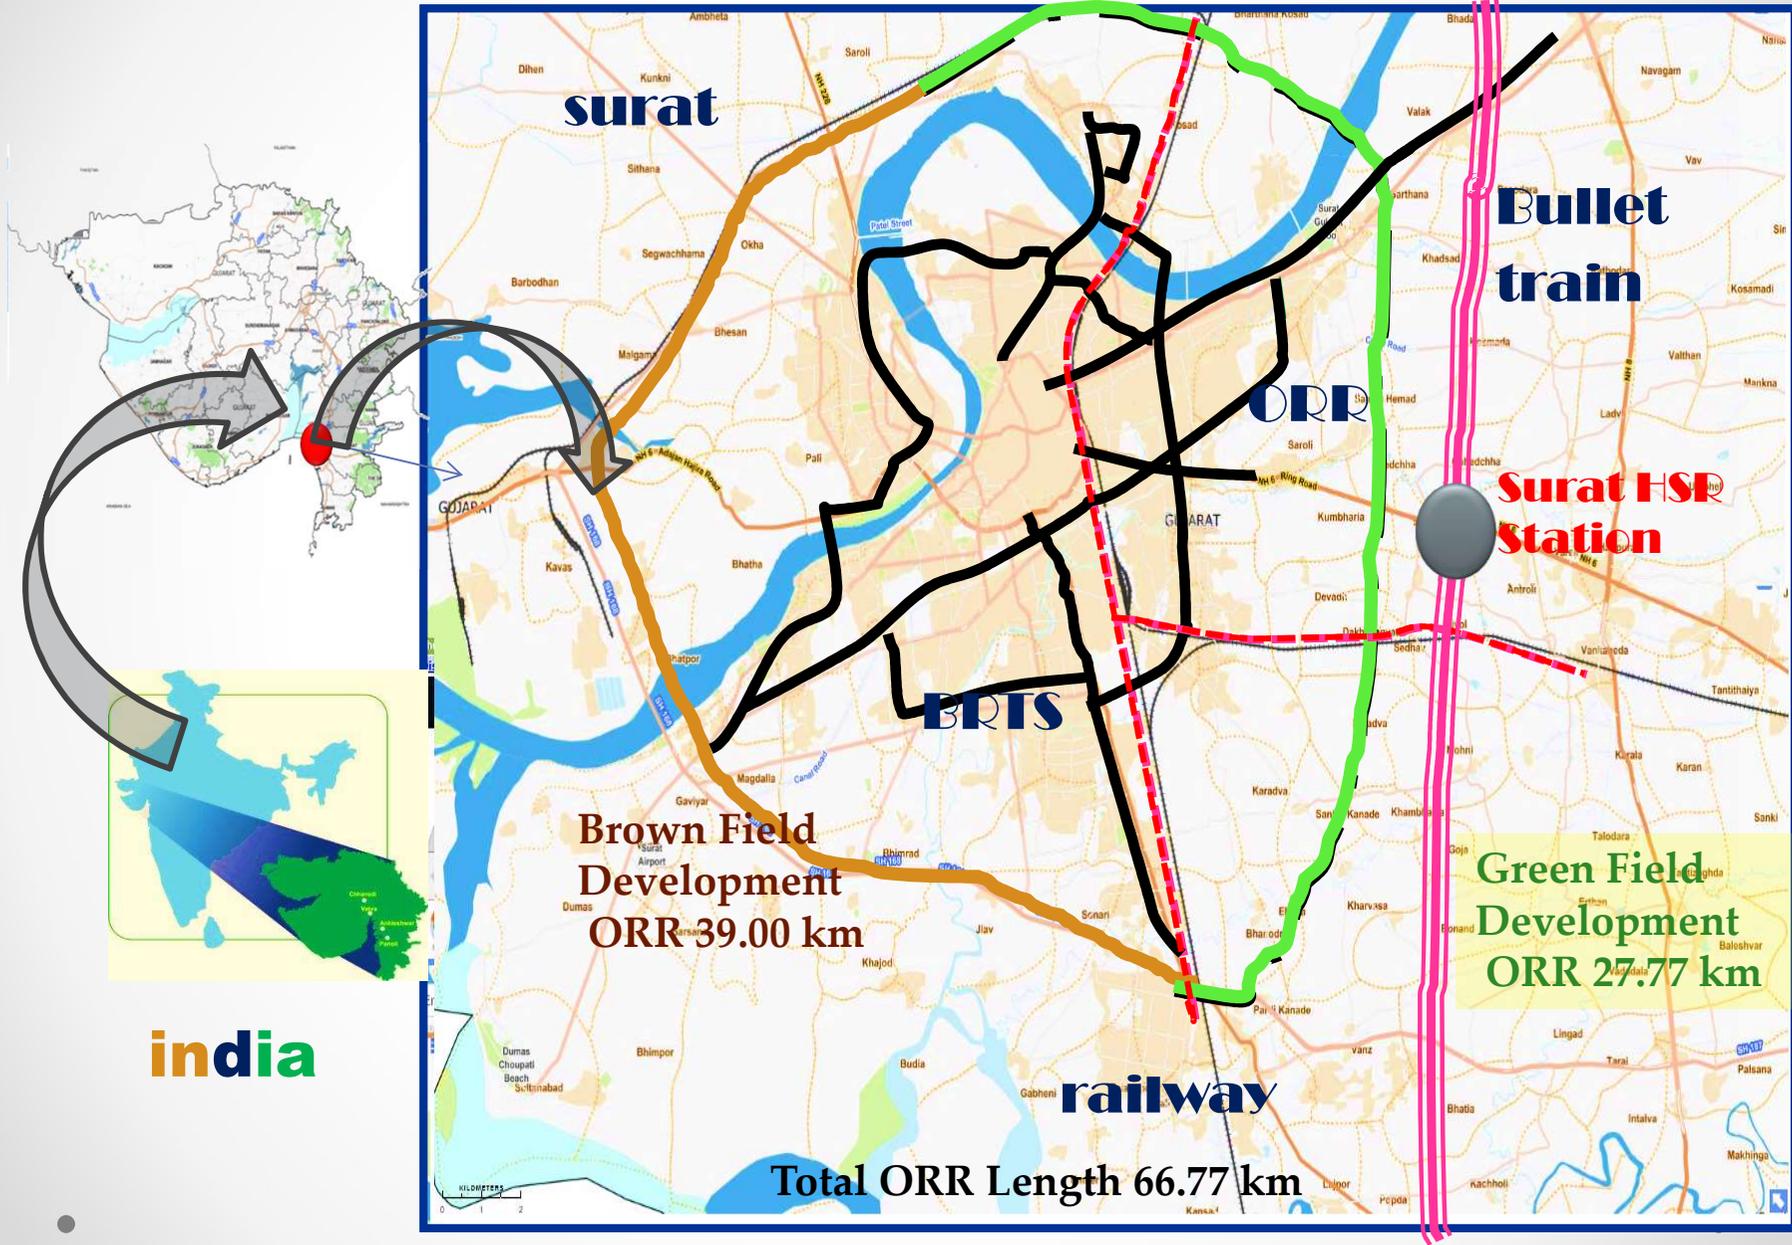


india

Total ORR Length 66.77 km

SURAT ORR CORRIDOR WITH PROVISION OF BRTS/MRTS

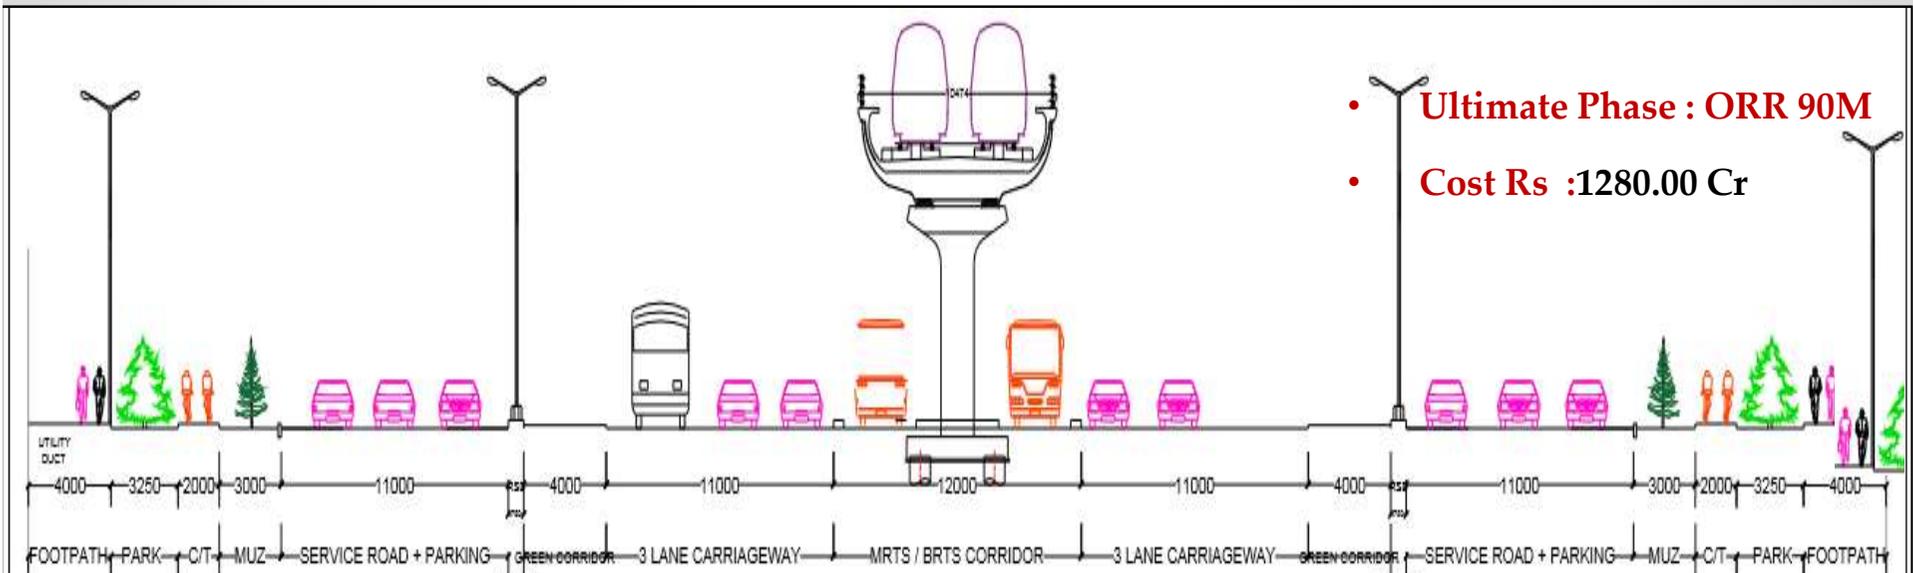

- **Ultimate Phase : ORR 90M**
- **Cost Rs :1280.00 Cr**

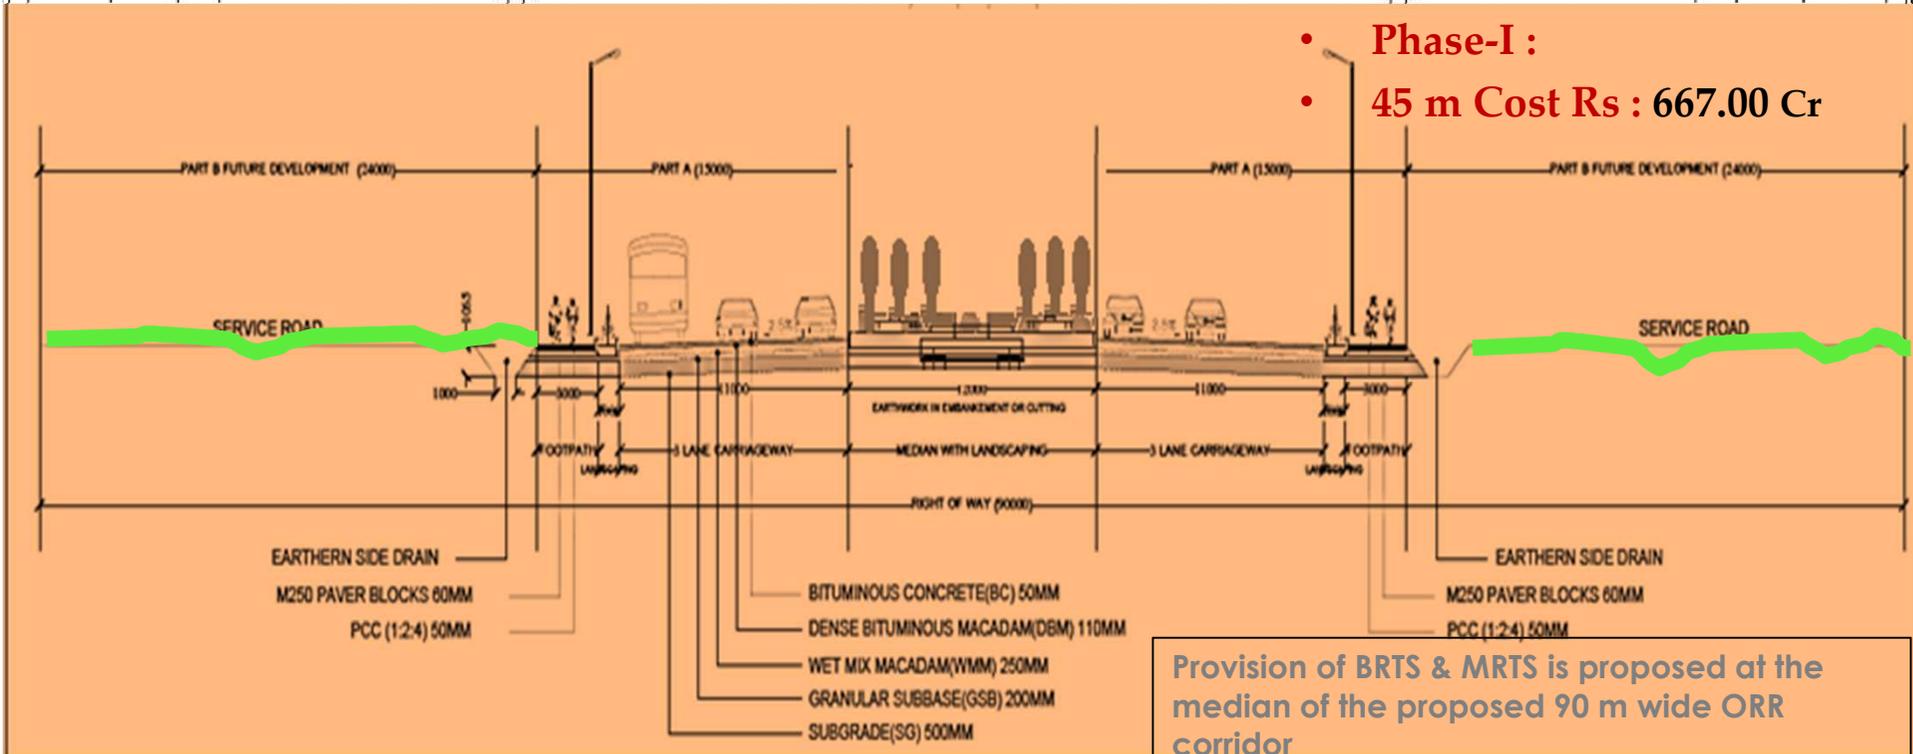


- **Phase-I :**
- **45 m Cost Rs : 667.00 Cr**

Provision of BRTS & MRTS is proposed at the median of the proposed 90 m wide ORR corridor

3D Virtual Model of ORR



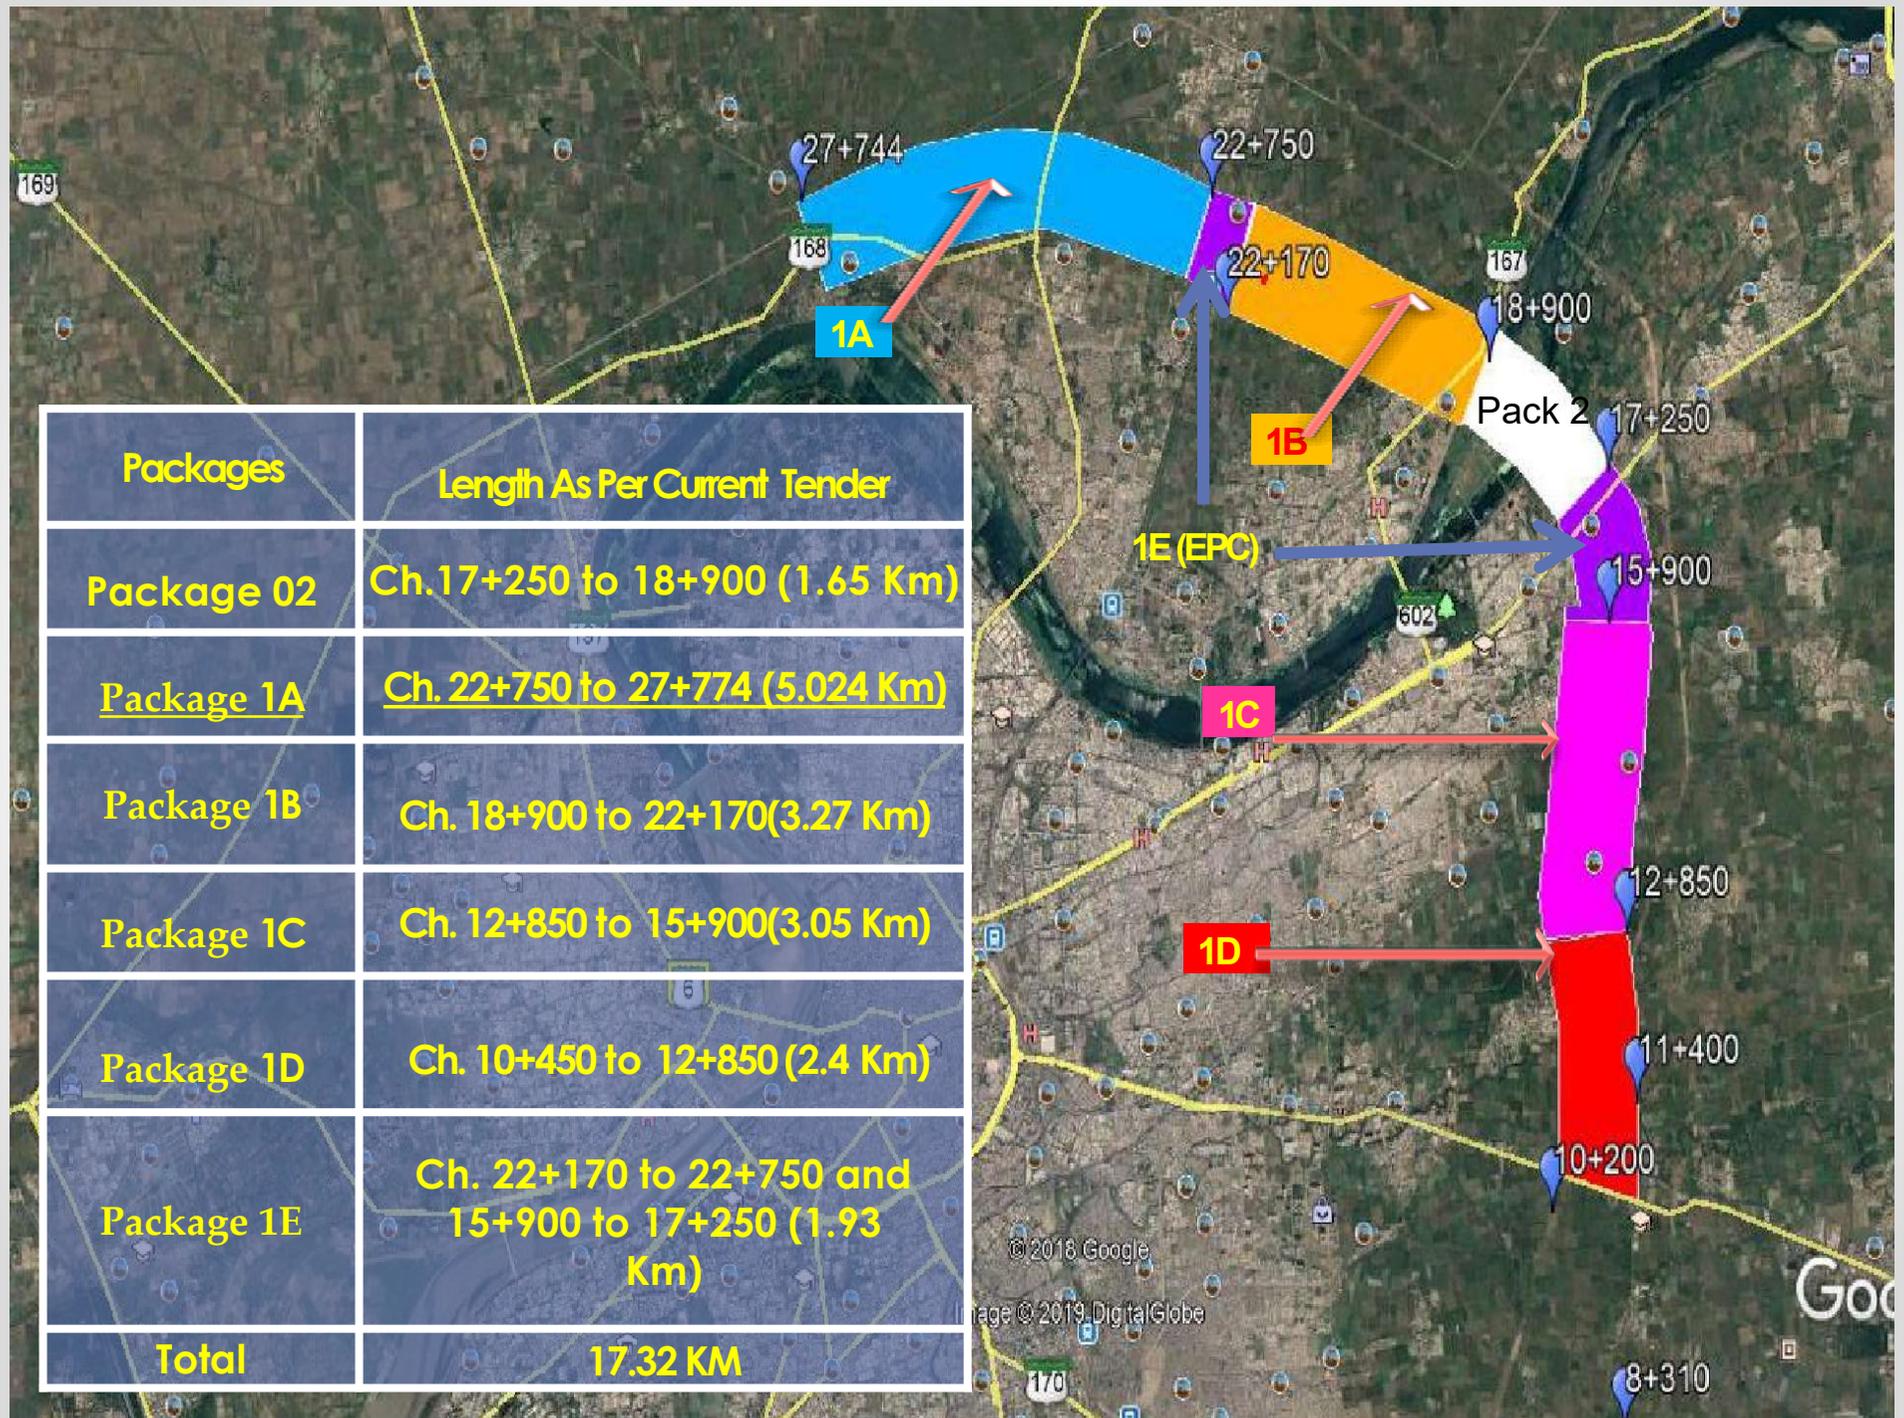

Packages	Length As Per Current Tender
Package 02	Ch. 17+250 to 18+900 (1.65 Km)
Package 1A	Ch. 22+750 to 27+774 (5.024 Km)
Package 1B	Ch. 18+900 to 22+170 (3.27 Km)
Package 1C	Ch. 12+850 to 15+900 (3.05 Km)
Package 1D	Ch. 10+450 to 12+850 (2.4 Km)
Package 1E	Ch. 22+170 to 22+750 and 15+900 to 17+250 (1.93 Km)
Total	17.32 KM

List Of On-Going Packages –Phase-01

Sr. No.	Package	Name of Work	Project Cost
1	Package 02	Construction for Major Bridge across River Tapi near Village Valak on Outer Ring Road Section at Surat on EPC Basis. (Design, Engineering, Procurement and Construction). (1.65km)	179.31 CR
2	Package 1A	Construction of 6 Lane (3+3) Outer Ring Road For Section Ch. 22+750 to 27+744 (5.024 Km) for URDCL, Surat Area	73.30 CR
3	Package 1B	Construction of 6 Lane (3+3) Outer Ring Road For Section Ch. 18+900 to 22+170 (3.27 Km) In URDCL, Surat Area	52.46 CR
4	Package 1C	Construction of 6 Lane (3+3) Outer Ring Road For Section Ch. 12+850 to 15+900 (3.05 Km) In URDCL, Surat Area	53.44 CR
5	Package 1D	Construction of 6 Lane (3+3) Outer Ring Road For Section Ch. 10+450 to 12+850 (2.4 Km) In URDCL, Surat Area	54.36 CR
6	Package 1E	Construction of Railway over Bridge , flyover, Underpass for 6 lane (3+3) Outer Ring Road For Section Ch. 22+170 to 22+750 & 15+900 to 17+250 (1.93 Km) In URDCL, Surat Area for EPC	73.57 CR
		TOTAL	486.44 CR

List of TP Scheme comes under the Current packages of ORR (17.32/27.77Km)

Sr.no	TP-No	TP-Scheme
1	TP- 51	Kosmada -Khadsad Pilodra-Simada –SUDA/SMC
2	TP- 52	Saniaahemad-Kosmada -Chhedchha –SUDA/SMC
3	TP- 53	Vedcha-Chhedchha - Sabaegam - Saniaahmad -SUDA
4	TP- 58	Valak –SMC
5	TP- 46	Gothan-Bharthana- Kosad-Variav- SMC
6	TP- 83	Variav- Kosad -SMC
7	TP- 84	Kosad- Bharthana-Mota Varacha-Abhrama-SMC
8	TP- 85	Sathana-pasodra-Laskana-SMC
9	TP-37	Variav-SMC
10	TP-38	Variav-SMC



Package 02 - Tapi River Bridge Valak




CONSTRUCTION OF TAPI RIVER BRIDGE NEAR VALAK VILLAGE, OUTER RING ROAD SURAT



CONSTRUCTION OF TAPI RIVER BRIDGE NEAR VILLAGE-VALAK, OUTER RING ROAD SURAT



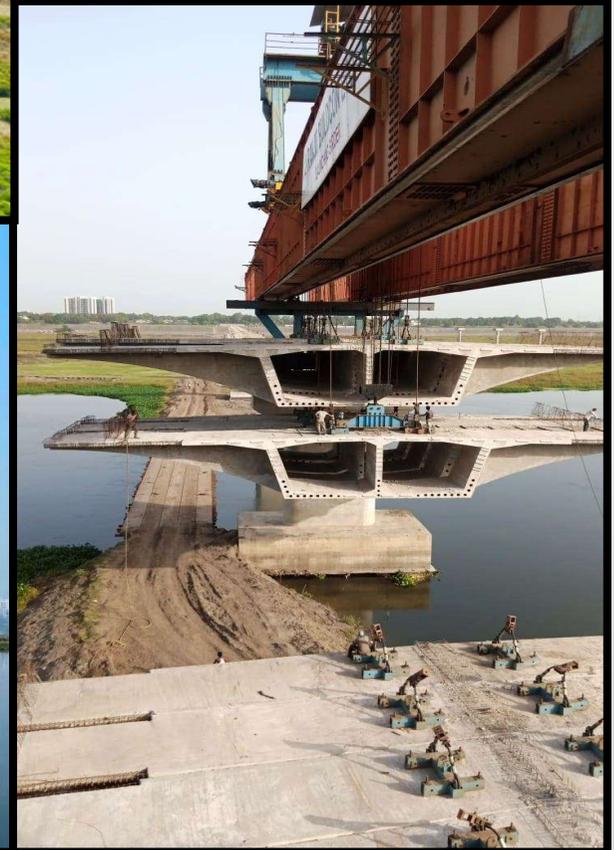

**Site Photos Tapi River Bridge of
Package 02**






Package- 1A



CONSTRUCTION OF ROAD NEAR KOSAD VILLAGE, OUTER RING ROAD SURAT




Site Photos of Package 1A

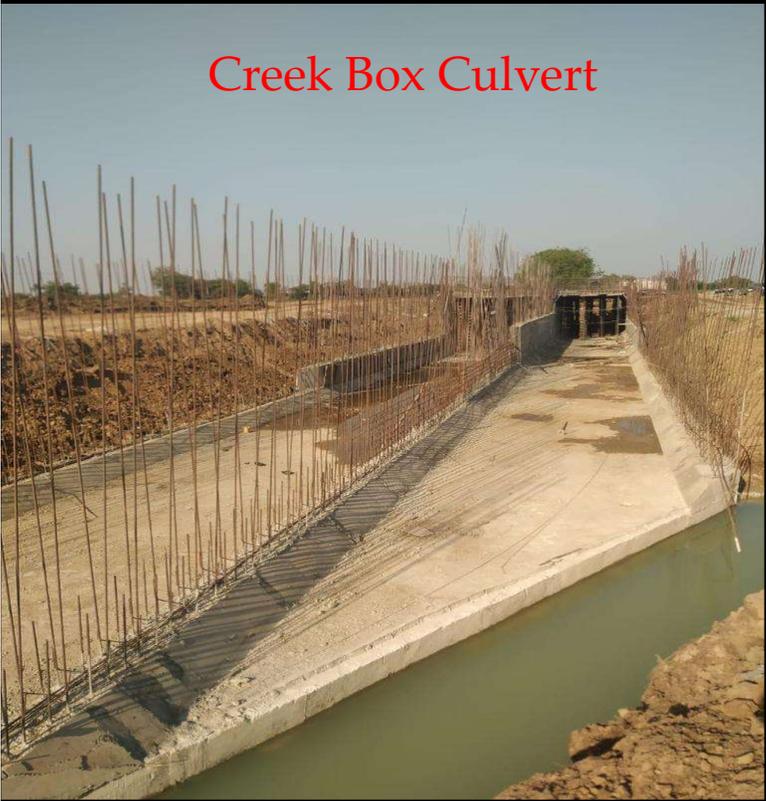


Creek Box Culvert



WMM 1st Layer

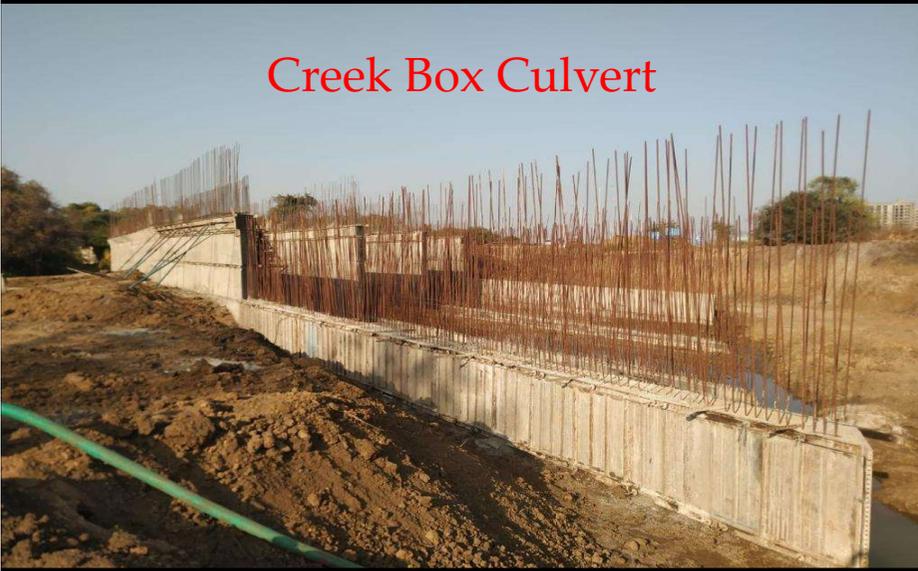

Creek Box Culvert

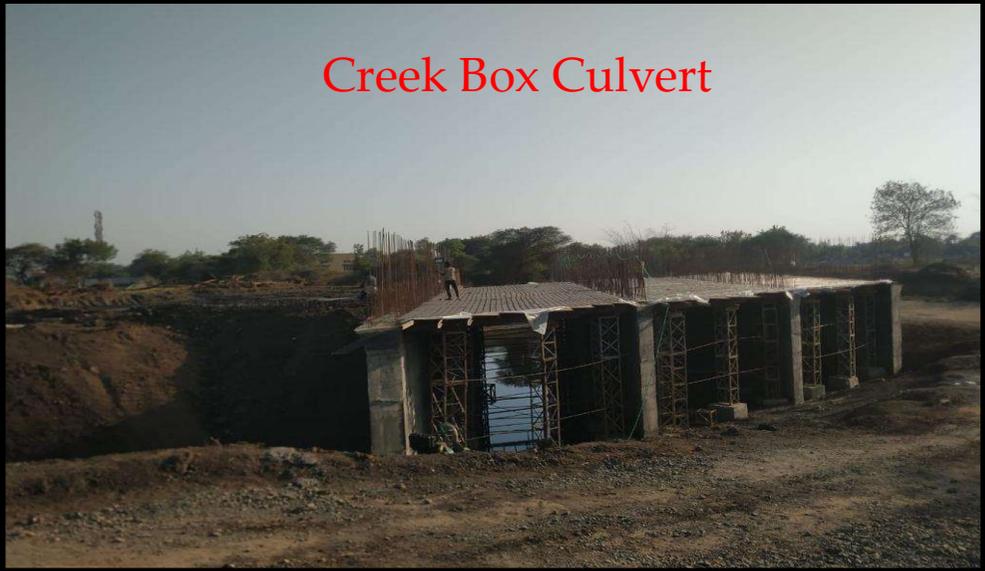

Creek Box Culvert



Package 1B



Site Photos of Package 1B



CONSTRUCTION OF ROAD NEAR MOTAVARACHA VILLAGE, OUTER RING ROAD



CONSTRUCTION OF ROAD NEAR ABRAMA VILLAGE, OUTER RING ROAD SURAT





Package 1C



Site Photos of Package 1C



CONSTRUCTION OF ROAD NEAR KOSMADA VILLAGE, OUTER RING ROAD SURAT



CONSTRUCTION OF ROAD NEAR KOSMADA VILLAGE, OUTER RING ROAD SURAT





Package 1D





Construction of creek structure at Sania Hemad, Outer Ring Road, Surat

Site Photos of Package 1D

Creek Diversion Work





Site Visit of Director (URDCL) on
Outer Ring Road @Package 1D

WMM 1st Layer



Creek Box Culvert

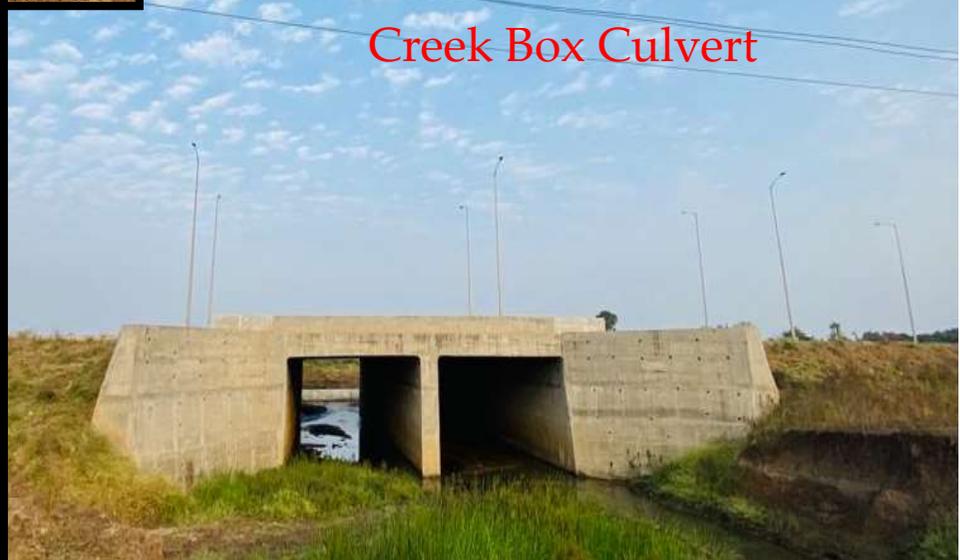

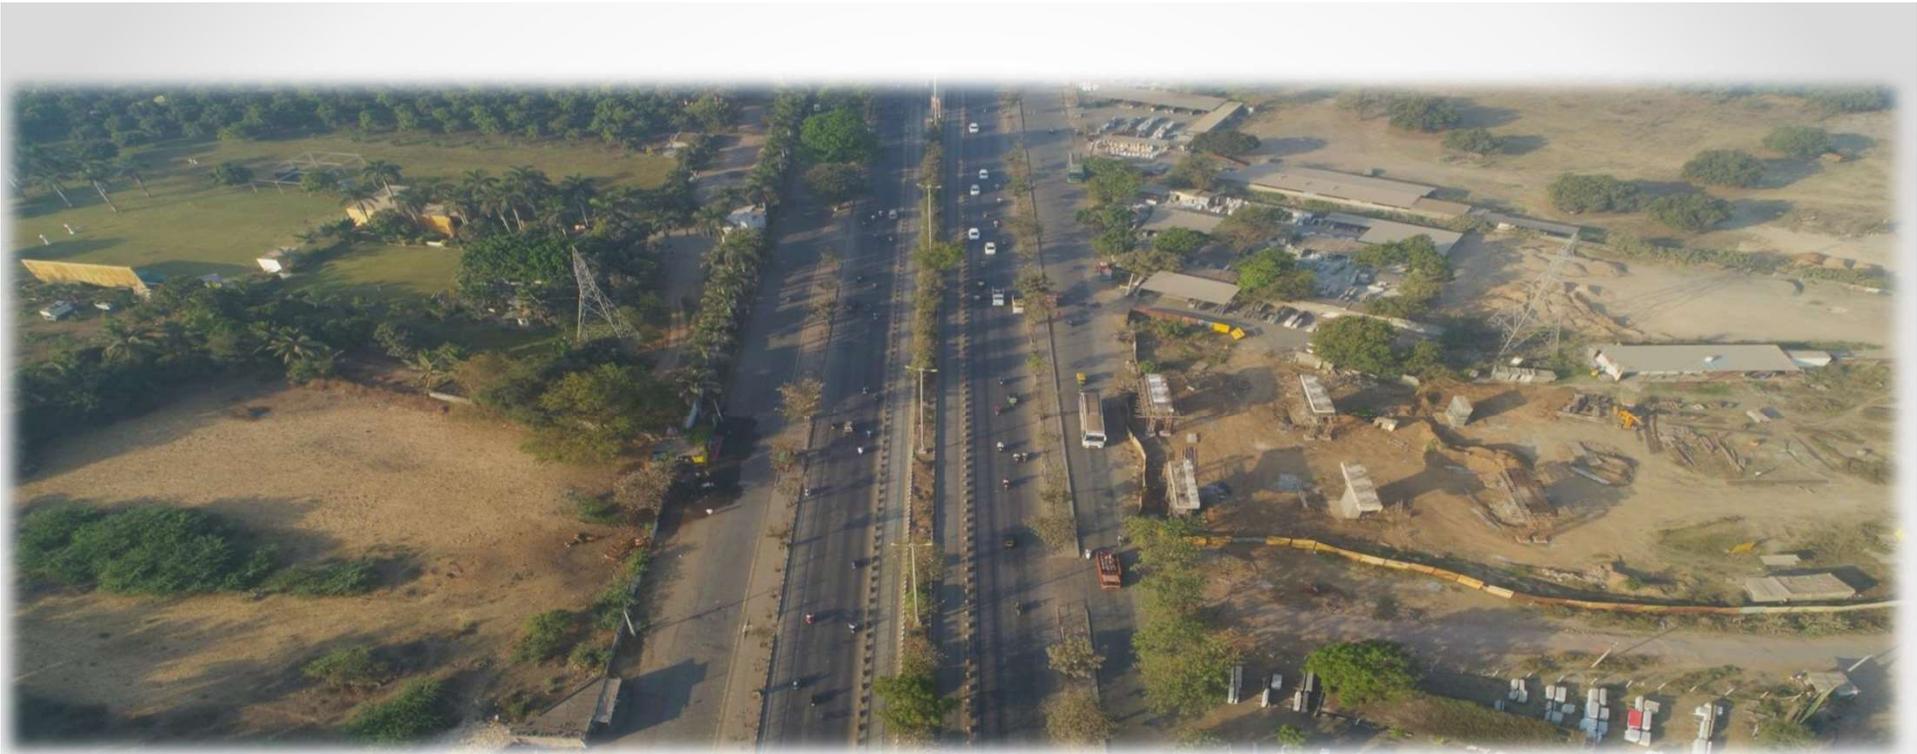

Package 1E (F.O.B,R.O.B,V.U.P)




Site Photos of Package 1E



Planning for remaining 10.45 Km Phase -1 (B)

Sr.no	Description	
1	Length	10.45km
2	Width (3+3 Lane + 12m Median)	45 m
3	Road length	6.45 km
	(including Road,Slip Road, 6 nos of Canal/Creek Structures)	
4	Structures length	5.2 Km
	2 nos of Flyover briges(1.2 km X 2 nos), 1 nos Railway over bridge((1.8km), Clover leaf at juntion(1.0 km)	
5	Cost of Road Work	125 Cr.
6	Cost of Structure Work	150 Cr.
	(FOB - (30 CrX 2), ROB - (40 Cr.), Clover Leaf (50 Cr.)	
7	Block Cost of 10.45 km	275 Cr
8	Anticipated Time for Completion	42 Months
9	TP Scheme include	
	TP- 53 To TP 57, TP 44, TP 59	7 Nos.



THANK YOU
